

QuickQuid

Engineering Handoff

**Most marketplaces help you hire.
QuickQuid helps the work get finished.**

Founding beta build guide for Product, Engineering, Design, Quality Assurance and Operations.

Kochi · UI/UX and frontend execution

Document Map

This document is the build contract. Product behavior, data, permissions and release gates are defined here.

Product Direction	4
Non-negotiable product decisions	4
Founding Beta Scope	5
Build now	5
Operationally manual	5
Not part of the founding beta	5
Public Website	6
Landing-page order	6
First fold	6
Readiness and Account Onboarding	7
Guest readiness conversation	7
Prepared summary	7
Access gate	7
QuickQuid Ready	8
AI-Assisted Matching	8
Matching sequence	8
Matching data	8
Buyer Experience	9
Pro Experience	9
Pact, Capacity and Commit Forecast	10
Capacity Lock	10
QuickQuid Pact	10
Commit Forecast	10
Changes, Delays and Delivery	10
Change Cards	11
Project Clock	11
First Proof	11
Definition of Done	12
Delivery Vault	12
Cashfree Milestone Payments	12
Commercial display	12
Cashfree capability rule	13
CashfreePaymentAdapter	13
Money authorization	13
Engineering references	14

Admin Operations	14
Queues	14
Separation of duties	14
Contextual Help	14
Canonical Records and States	15
Minimum records	15
Core states	15
Security, Privacy and Reliability	15
Critical Edge Cases	16
Identity and onboarding	16
Project and matching	16
Money	16
Delivery and dispute	17
Build Order	17
Phase 1 - Foundation	17
Phase 2 - Readiness and onboarding	17
Phase 3 - Marketplace	17
Phase 4 - Execution	17
Phase 5 - Cashfree sandbox	18
Phase 6 - Founding beta hardening	18
Release Checklist	18
Product gates	18
Commercial and Cashfree gates	18
Operations and quality gates	18
Founding Beta Measures	19
Glossary	20

Product Direction

QuickQuid is an execution marketplace for digital work.

Most marketplaces help you hire. QuickQuid helps the work get finished.

The product is designed around a simple outcome: a Buyer arrives with unfinished work and leaves with accepted, properly handed-over work. Profiles, proposals, chat and payments exist to support that outcome. They are not the product by themselves.

The founding beta starts in Kochi with UI/UX and frontend work. Backend, mobile and AI/ML remain configurable categories but stay closed until QuickQuid has the right reviewers, proof standards, delivery standards and supply.

Non-negotiable product decisions

- QuickQuid charges Buyers and Pros a platform fee of ₹0 during the founding beta.
- A guest can prepare a project without creating an account.
- A guest cannot enter Buyer or Pro workspaces.
- A project cannot enter matching until it passes QuickQuid Ready.
- Matching must consider relevant proof, real capacity, budget and timing.
- AI assists matching; it does not approve projects, select the winning Pro or move money.
- The Buyer and Pro accept the same Pact before payment and work begin.
- Chat cannot change scope. Approved Change Cards change scope.
- A Pro cannot start work until the milestone payment is confirmed and the milestone is unlocked.
- Delivery, revisions, acceptance, delays and money actions are recorded against canonical states.
- Cashfree is the payment provider.
- The word “escrow” is used only when Cashfree One Escrow is enabled for QuickQuid and the wording is approved by Legal.
- Q₹ is demo-only currency with no cash value.



The QuickQuid execution lifecycle

Founding Beta Scope

Build now

Product area	Required capability
Public website	Clear execution proposition, selected beta tracks and one main Buyer CTA
Readiness	Guest conversation, progress, prepared summary and QuickQuid review
Accounts	Authentication, Buyer and Pro onboarding, role and object authorization
Marketplace	Proof profiles, capacity, AI-assisted shortlist, proposals and productized gigs
Agreement	QuickQuid Pact, milestones, Scope Snapshot and Commit Forecast
Execution	Workroom, First Proof, Change Cards, Project Clock and Definition of Done
Delivery	Versioned delivery, protected files/links, review, revision and acceptance
Money	Cashfree sandbox checkout, milestone ledger, payout/refund states and reconciliation
Operations	Admin queues, role separation, maker-checker, SLA clocks and audit events
Closeout	Reviews, rehire and execution outcome records

Operationally manual


The following decisions may be performed by the team during the beta, but every decision must exist inside the product with an owner, state, reason, evidence and timestamp:

- Ready review.
- Project Archetype approval.
- Match shortlist approval.
- Funding unlock.
- Payout and refund authorization.
- Dispute mediation.
- Trust and Safety decisions.
- Reconciliation exceptions.
- Privacy export and deletion review.

Not part of the founding beta

- Enterprise accounts, Teams and TDS overlays.
- Offline payments, cheque workflows and manual bank-statement matching.
- Wallets or withdrawable Q₹ balances.
- Paid placement, promoted gigs and priority feeds.
- Automated Pro selection or autonomous AI routing.
- Automated risk decisions.
- Replacement guarantees, zero-risk claims or guaranteed completion dates.
- Flex Pool, Relay, Execution Passport and advanced benchmark engines.

YAGNI rule: if a capability does not help a Buyer complete the first paid project, help a Pro deliver it, or help Operations safely resolve it, it does not ship in the founding beta.

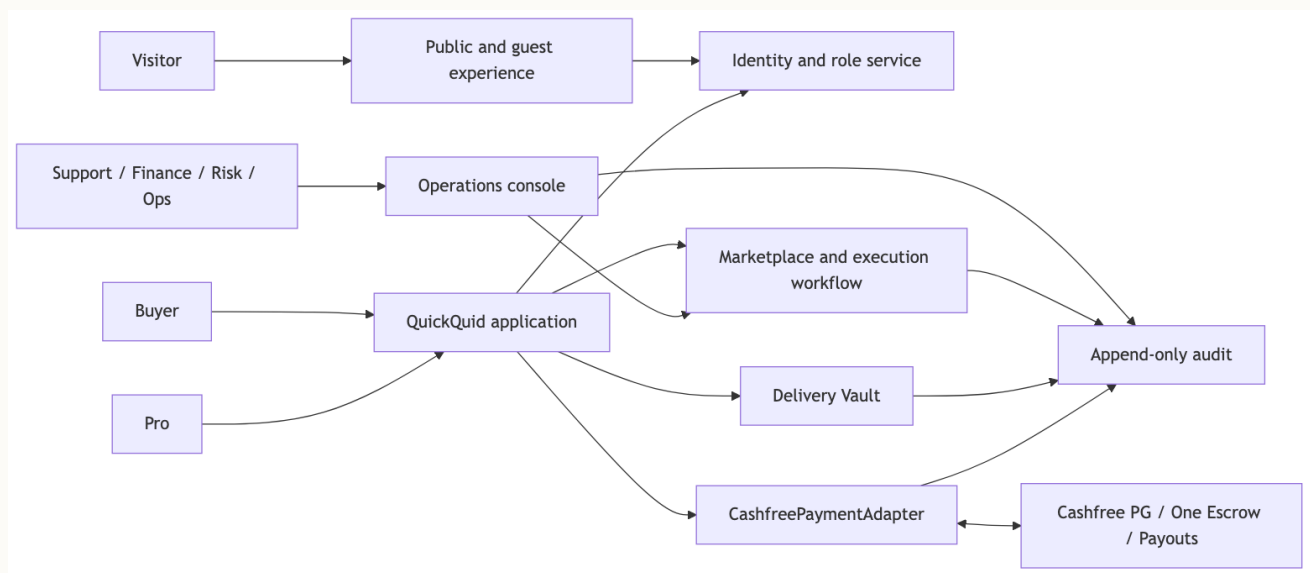

Product and operating boundary

Public Website

The website is a conversion surface, not a product manual. It should contain only the information needed to understand the promise, trust the process and start.

Landing-page order

- 1 Hero request input.
- 2 Selected beta tracks.
- 3 Five-stage execution journey.
- 4 Why execution is different.
- 5 One clearly labelled example outcome.
- 6 Buyer and Pro entry paths.
- 7 Final CTA and Help link.

First fold

Element	Required content
Eyebrow	Founding beta · Kochi
Headline	Most marketplaces help you hire. QuickQuid helps the work get finished.
Supporting line	Turn a rough request into a Ready project, match on proof and capacity, and run the work through clear scope, checkpoints and acceptance.
Input label	What needs to get finished?
Example	Redesign our onboarding and deliver editable Figma files in three weeks
Main action	Check project readiness
Trust line	No account needed to start. QuickQuid reviews the project before matching.

Use one dominant Buyer action. Repeat it only after the process explanation and at the end of the page. Do not use fabricated activity counters, customer logos, ratings, testimonials, deadlines or project claims.

Readiness and Account Onboarding

The readiness journey is the public entry point for Buyers.



Readiness and account gate

Guest readiness conversation

The guest answers seven areas:

- 1 Outcome and category.
- 2 Deliverables and exclusions.
- 3 Inputs and dependencies.
- 4 Budget.
- 5 Target date and deadline reason.
- 6 Decision-maker and feedback window.
- 7 Acceptance and handoff criteria.

The assistant may structure an answer, identify a gap and suggest wording. Any inferred information must be visibly marked and editable. The assistant must not call the project Ready, approve a date, select a Pro or create an account.

Use these readiness labels:

- MISSING
- ANSWERED
- NEEDS_CONFIRMATION
- PREPARED_FOR_REVIEW

Prepared summary

After the seven areas are complete, show one editable project summary. Its label is **Prepared for QuickQuid review**.

The primary action is **Create account and save project**. Sign-in is available for an existing Buyer. The project must remain a guest draft until authentication and minimal Buyer onboarding are complete.

Access gate

Buyer workspace access requires:

`authenticated = true AND activeRole = BUYER AND buyerProfileComplete = true`

Pro workspace access requires:

`authenticated = true AND activeRole = PRO AND proProfileComplete = true`

The readiness draft must survive refresh, sign-in, account creation and onboarding. It attaches to the Buyer exactly once. If restore fails, show retry and a support reference instead of opening an empty dashboard.

QuickQuid Ready

A project cannot enter matching until the reviewed project version passes every required check:


- Clear outcome and Project Archetype.
- Deliverables and exclusions.
- Inputs, access and dependencies.
- Budget and funding approach.
- Named Buyer decision-maker.
- Target date and deadline reason.
- Buyer feedback window.
- Acceptance and handoff criteria.
- AI-use policy: OPEN, DISCLOSE, APPROVED_TOOLS or CONFIDENTIAL.

An authorized Operations user approves or returns the review. A failed review records the gap, reason, owner and next action. A material edit after approval creates a new project version and returns it to review.

Projects in DRAFT, READINESS_REVIEW or NOT_READY are never visible to Pros and never enter matching.

AI-Assisted Matching

Matching begins only for a frozen READY project version.



AI-assisted matching with human control

Matching sequence

- 1 **Hard eligibility filter** - active Pro, allowed category, required verification dimensions, no restriction or conflict, correct opportunity visibility and minimum capacity.
- 2 **AI retrieval and ranking** - compare the project archetype, scope and constraints with structured proof, comparable outcomes and stated work preferences.
- 3 **Deterministic checks** - validate weekly capacity, budget compatibility, timing and any relevant location rules.
- 4 **Admin review** - Operations approves, edits or rejects the candidate set with a reason.
- 5 **Buyer shortlist** - show three to five approved Pros with proof, availability, uncertainty and a plain-language explanation.
- 6 **Buyer selection** - the Buyer chooses a Pro or asks QuickQuid for another option.
- 7 **Outcome capture** - record selection, decline, start, acceptance, dispute and rehire outcomes.

Never show a fabricated match percentage. The Buyer should understand why each person is suitable and what remains uncertain.

Matching data

Store:

- MatchRun: project version, model version, prompt/template version, policy version, status and timestamps.
- MatchCandidate: Pro, hard-filter result, proof references, capacity result, rank band and exclusion reason.
- MatchExplanation: project-specific reasons, evidence references and uncertainty.

- MatchReviewDecision: Admin, final order, approval/edit/rejection reason and timestamp.

Do not use protected characteristics, raw KYC documents, bank details, private contact information or unrelated message content as matching inputs. If the matching service fails, create a manual matching case. The project remains usable.

Buyer Experience

The Buyer workspace should be calm and task-led. The dashboard shows one primary next action, active projects and important alerts. It should not attempt to display every feature at once.

Surface	Required behavior
Dashboard	Derive each project status and next action from canonical records
Projects	List owned drafts, projects and active contracts; keep Create project separate
Project editor	Restore readiness answers and use short saved sections
Matches	Show only the approved project-specific shortlist with proof and reasons
Proposals	Bind proposals to the current project version
Pact	Show scope, duties, dates, acceptance criteria and the exact revision being accepted
Payment	Show professional fee, QuickQuid fee ₹0, provider charge, tax placeholder and total
Workroom	Show the active scope, Clock, checkpoint, delivery versions and next valid action
Messages	Keep messages contextual; use Change Cards for scope changes
Support	Create an entity-linked case with the minimum required context
Profile	Keep public identity separate from billing and legal information

Productized gigs are allowed. A gig request creates a private project draft using an immutable snapshot of the offer, then follows the same Ready, matching, Pact, execution and payment lifecycle.

Pro Experience

Pro readiness is multidimensional. Do not use one universal verified flag.

Track separately:

- Account and contact readiness.
- Identity/KYC review.
- Public profile completion.
- Category eligibility.
- Proof evidence.
- Weekly capacity.
- Payout readiness.

Surface	Required behavior
Dashboard	Show capacity, invitations, active work, blockers and one primary next action
Profile	Separate Identity, Proof, Capacity and Payout/KYC stages
Opportunities	Show only invited or eligible READY projects
Proposals	Bind price, timing, proof and capacity to the current project version

Surface	Required behavior
Gigs	Show title, status, active requests and next action; keep analytics secondary
Pact	Accept the same revision as the Buyer and create one capacity lock
Workroom	Enable work only after confirmed funding and milestone unlock
Delivery	Submit immutable versions against acceptance criteria and Definition of Done
Payouts	Show Cashfree payout state, settlement state and the exact recovery action

Pact, Capacity and Commit Forecast

Capacity Lock

Store each Pro's weekly available hours. Subtract existing commitments week by week. Compare remaining capacity with the project effort plan for every affected week. Do not average capacity across weeks to hide a shortfall.

Accepted work creates a capacity commitment. If capacity changes before Pact acceptance, recalculate before either party can accept.

QuickQuid Pact

The Buyer and Pro accept the same Pact revision. It contains:

- Deliverables and exclusions.
- Milestones and prices.
- Buyer input and access dates.
- Buyer feedback windows.
- Pro checkpoints and delivery duties.
- Blocker-response expectations.
- AI-use and confidentiality rules.
- Commit Forecast assumptions.
- Definition of Done template.


Acceptance creates an immutable Scope Snapshot.

Commit Forecast

The forecast uses milestone effort, weekly capacity, dependency dates and agreed response windows. It is an evidence-based expected date, not a guarantee.

Recalculate after an approved Change Card, a material Delay Event, an agreed dependency change or a capacity-affecting pause.

Changes, Delays and Delivery

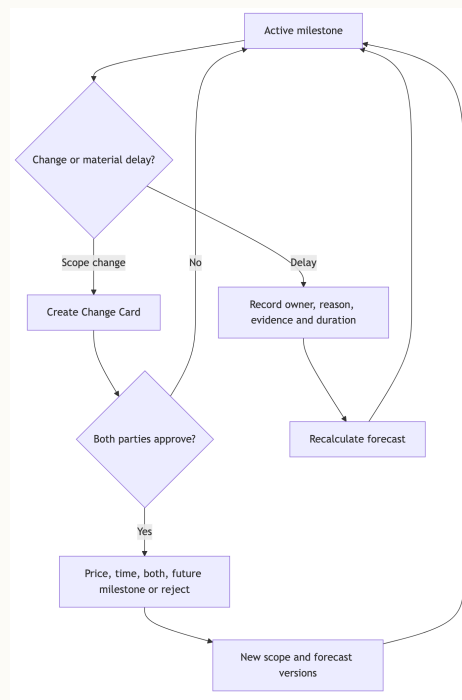

Scope and delay control

Change Cards

Active scope changes require an approved Change Card. Allowed outcomes:

- Add price and retain time.
- Add time and retain price.
- Add price and time.
- Move work to a future milestone.
- Reject the change.

Approval creates a new scope version and, when required, a new Commit Forecast. Chat messages have no scope effect.

Project Clock

Every material delay records:

- Owner: BUYER, PRO, QUICKQUID or EXTERNAL.
- Affected milestone.
- Start, end and duration.
- Reason and evidence.
- Forecast impact.
- Creator and approval history.

Delay ownership describes what happened. It does not automatically create a penalty.

First Proof

Require an early proof when it is the Pro's first QuickQuid project, a new project archetype for the Pro, or an Operations-identified risk. A proven repeat engagement may receive a recorded waiver.

Definition of Done

UI/UX delivery requires editable source files, exports, assets, fonts/licences, component guidance and handoff notes.

Frontend delivery requires a working build, agreed responsive behavior, required tests, repository access, environment-variable documentation without secrets, deployment/rollback instructions, credential ownership transfer and known-issue disclosure.

Acceptance is blocked while any required check is incomplete.

Delivery Vault


The Delivery Vault is the protected record for milestone evidence and handoff material. It is not a general file drive.

Required behavior:

- Validate file type and size.
- Scan supported uploads before review.
- Record checksum and processing state.
- Use private storage and short-lived authorized access.
- Allow draft replacement before submission.
- Freeze submitted versions.
- Preserve prior versions after a revision.
- Bind comments, revisions and acceptance to an exact version.
- Prevent acceptance of a superseded version.
- Freeze affected evidence when a dispute opens.
- Never publish private delivery to a portfolio automatically.

Buyer and Pro access is contract-scoped. Support and Risk access is case-scoped. Finance sees metadata by default. Every preview and download is authorized server-side.

Cashfree Milestone Payments



Cashfree milestone payment and payout flow

Commercial display

Line item	Founding beta rule
Professional fee	Agreed project or milestone amount
Buyer QuickQuid fee	₹0
Pro QuickQuid fee	₹0
Cashfree/provider charge	Separate when known
Applicable tax	Separate placeholder until approved
Checkout total	Professional fee + provider charge + approved tax

Money is stored as integer minor units with an explicit currency. No floating-point calculations.

Cashfree capability rule

Enabled capability	Product behavior	Customer wording
Payment Gateway	Collect milestone payment and update the internal funding ledger	Milestone payment or funding confirmed
Easy Split/deferred settlement	Split and schedule eligible settlement	Protected milestone funding or scheduled settlement
One Escrow	Approved escrow-account flow with agreed release conditions	Escrow only after Legal approval
Payouts	Execute an authorized Pro payout or refund	Requested, processing, settled or failed according to state

Easy Split is not presented as escrow. Settlement windows and eligibility come from the QuickQuid Cashfree account configuration and must not be hard-coded.

CashfreePaymentAdapter

The adapter must:

- Create a Cashfree order and hosted checkout.
- Query payment state.
- Verify webhook signatures using the raw request body.
- Store multiple attempts for one order_id using distinct cf_payment_id values.
- Treat only the documented terminal success state as paid.
- Normalize payment, refund, payout and settlement events.
- Handle duplicates and out-of-order events safely.
- Create authorized payout/refund instructions.
- Track settlement and reconciliation.
- Keep sandbox and live credentials/data separate.
- Expose enabled capability flags.

There is no Buyer-entered UTR, NEFT/IMPS matcher, offline instrument, cheque-bounce workflow or manual payout batch.

Money authorization

- Payment success and milestone unlock are separate facts.
- Work begins only after both facts are valid.
- Buyer acceptance creates one payout intent; it does not move money.
- Finance authorizes payout/refund actions.
- Cashfree executes the transfer.
- Risk decides dispute outcomes.
- A mismatch creates a Finance case and never silently changes internal records.
- Every command uses an idempotency key.


Real money remains disabled until the Cashfree products, contracts, production credentials, Legal wording, tax treatment, KYC policy, maker-checker thresholds and refund/dispute policy are approved.

Engineering references

- [Cashfree Easy Split](#)
- [Cashfree One Escrow](#)
- [Cashfree payment webhooks](#)
- [Cashfree webhook idempotency](#)
- [Cashfree Payouts](#)

Admin Operations

Admin is an operating console, not a universal bypass.



Admin decision and maker-checker flow

Queues

Queue	Owner	Exit condition
Profile and verification	Operations	Approved, changes requested or restricted
Ready review	Operations	READY or NOT_READY
Matching	Operations	Approved shortlist shared or no-fill escalated
Money exception	Finance	Reconciled, safely retried, refunded or escalated
Dispute	Risk	Decision recorded and execution assigned
Trust and Safety	Risk	Restriction, restoration or closure
Privacy	Authorized Operations	Fulfilled, partly deferred or rejected with reason
SLA breach	Operations lead	Reassigned, escalated or resolved

Separation of duties

- Operations reviews readiness, proof and assignments.
- Support handles routine help and onboarding context.
- Finance authorizes and executes approved money operations through Cashfree.
- Risk decides disputes, restrictions and Trust and Safety cases.
- Engineering receives masked diagnostics by default.
- The maker and checker for a sensitive action must be different people.

Sensitive reveal requires a reason, recent reauthentication, a time-limited view and an audit event. Data remarks automatically.

Contextual Help

Help should understand the current screen and task. A support case may attach the current route, actor, entity ID, state, correlation ID and a user-selected screenshot or file.

Do not automatically attach full conversations, KYC history, bank data, complete payment history or unrelated project records.

Canonical Records and States

The backend record is authoritative. Dashboard labels and next actions are derived views.

Minimum records

- Identity: Account, Person, Organization, Membership, RoleCapability.
- Profiles: BuyerProfile, ProProfile, VerificationDimension.
- Project: GuestReadinessDraft, Project, ProjectVersion, ProjectReadinessReview.
- Matching: ProjectArchetype, ProofMatchEvidence, MatchRun, MatchCandidate, MatchExplanation, MatchReviewDecision.
- Capacity and agreement: CapacityPlan, CapacityCommitment, Proposal, ExecutionPact, Contract, Milestone.
- Execution: CommitForecast, ScopeSnapshot, ChangeCard, DelayEvent, FirstProof, DefinitionOfDoneCheck.
- Delivery: DeliveryUpdate, VaultAsset, VaultGrant, VaultReview.
- Money: PaymentIntent, ProviderPayment, PayoutIntent, RefundIntent, ProviderEvent, ReconciliationRun.
- Operations: Dispute, AdminCase, AuthorizationDecision, SlaClock, AuditEvent.
- Outcome: ExecutionOutcome, Review, RehireLink.

Core states

Entity	States
Project	DRAFT, READINESS_REVIEW, NOT_READY, READY, MATCHING, PACT_PENDING, ACTIVE, PAUSED, IN_REVIEW, COMPLETED, CANCELLED, DISPUTED
Contract	DRAFT, PACT_PENDING, ACCEPTED_PENDING_FUNDING, ACTIVE, PAUSED, IN_REVIEW, COMPLETED, CANCELLED, DISPUTED
Milestone	DRAFT, FUNDING_REQUIRED, FUNDED, ACTIVE, FIRST_PROOF_REVIEW, DELIVERY_SUBMITTED, REVISION_REQUIRED, ACCEPTED, PAYOUT_QUEUED, PAID, DISPUTED
Payment	CREATED, CHECKOUT_OPEN, PROCESSING, SUCCEEDED, FAILED, CANCELLED, EXPIRED
Payout	NOT_READY, QUEUED, AUTHORIZATION_PENDING, RELEASE_REQUESTED, SETTLING, SETTLED, FAILED, HELD
Dispute	OPEN, RESPONSE_DUE, MEDIATION, DECIDED, EXECUTION_PENDING, CLOSED

Every transition specifies the current state, trigger, actor, preconditions, resulting state, side effects, notification, recovery path, timestamp and correlation ID. Stale actions are rejected. Immutable history is corrected with new events, not edits.

Security, Privacy and Reliability

- Enforce role and object authorization on every backend read and write.
- Require 2FA for Admin roles.
- Reauthenticate sensitive Admin actions.

- Encrypt traffic and protected data.
- Mask identity and financial fields in routine views and logs.
- Store secrets outside application code.
- Rate-limit authentication, readiness, messaging, upload and webhook endpoints.
- Use private storage and short-lived Vault access.
- Scan uploads before review.
- Keep sandbox, test and live data separated.
- Support authenticated privacy export and deletion cases.
- Redact third-party data from exports.
- Keep audit events append-only.
- Retry background work with bounded backoff and visible dead-letter failures.
- Connect frontend, backend, job, webhook and audit activity with correlation IDs.

Core journeys must work by keyboard, with a screen reader, at 200% zoom and at 320px width. Every screen needs loading, empty, validation, permission-denied, pending, failure and recovery states.

Critical Edge Cases

Identity and onboarding

- Guest opens a protected route: preserve safe intent, authenticate and return only when authorized.
- Existing email: offer sign-in instead of creating a duplicate identity.
- Session expires mid-form: preserve the non-sensitive draft and return to the same step.
- Wrong role: allow correction before the first role-specific submission.
- Suspended user with active work: block new activity but preserve permitted obligation, evidence and appeal access.

Project and matching

- Two tabs edit the same project: reject the stale save and offer reload/compare.
- Ready project changes materially: create a new version and reopen review.
- AI matching is unavailable: create a manual matching case.
- No candidate passes hard rules: record no-fill reason and let Operations revise criteria or source manually.
- Capacity changes before Pact: recalculate before acceptance.
- Old proposal or Pact revision: reject and show the current version.

Money

- Checkout expires: leave the milestone unfunded and permit a new payment intent.
- Invalid signature: no domain transition.
- Duplicate webhook: return success without repeating side effects.
- Out-of-order event: store, apply only legal transitions and reconcile.
- Amount/currency mismatch: quarantine and open a Finance case.
- Cashfree succeeds after browser timeout: reconcile; do not create a second charge.
- Payout command times out: query Cashfree before retrying with the same idempotency key.

- Settlement or refund fails: preserve the exact provider result and keep the case open.
- Chargeback after payout: open Finance/Risk cases without rewriting settled history.

Delivery and dispute

- Unsupported, executable, infected or unscannable file: reject before review.
- Interrupted upload: resume or restart without creating a reviewable duplicate.
- Comment on an old version: reject and return to the current version.
- Acceptance and dispute arrive together: serialize the transitions; a valid dispute prevents payout queuing.
- One milestone is disputed: freeze only the affected evidence and money unless Risk records a broader hold.
- Deletion request during an active obligation: delete eligible data and defer required records with a reason.

Build Order

Phase 1 - Foundation

- Authentication, roles, organizations and profiles.
- Backend object authorization.
- Admin capabilities, 2FA, queues, SLA clocks and audit events.
- Configuration for categories, policies, Cashfree environments and limits.

Exit: negative authorization and audit tests pass.

Phase 2 - Readiness and onboarding

- Guest readiness conversation.
- Prepared summary and account gate.
- Minimal Buyer onboarding.
- Draft preservation, attachment and recovery.

Exit: a guest cannot enter the Buyer workspace and a prepared draft attaches exactly once.

Phase 3 - Marketplace

- Buyer projects and Ready review.
- Pro proof, capacity, opportunities and proposals.
- Hard filters, AI ranking, Admin matching review and Buyer shortlist.
- Pact, capacity lock and Commit Forecast.
- Productized gig requests entering the same lifecycle.

Exit: a brief or gig request reaches a valid Pact without bypassing Ready or capacity.

Phase 4 - Execution

- Milestones, Scope Snapshot, Project Clock and First Proof.
- Workroom, Change Cards and Definition of Done.
- Delivery Vault, revisions, acceptance, reviews and rehire.
- Dispute evidence containment.

Exit: the complete execution loop passes using Q₹ demo currency.

Phase 5 - Cashfree sandbox

- Cashfree checkout and normalized webhook handling.
- Milestone funding ledger.
- Refund, payout and settlement tracking.
- Finance authorization and reconciliation exceptions.

Exit: contract tests and daily reconciliation pass in sandbox. No screen requests UTR or manual bank evidence.

Phase 6 - Founding beta hardening

- Accessibility, responsive behavior and performance.
- Privacy cases, appeals and Trust and Safety recovery.
- Alerts, backups, restore testing and operating runbooks.
- Demo-data isolation and analytics verification.

Exit: the release checklist passes and all production-money gates are approved.

Release Checklist

Product gates

- ☐ Readiness cannot open Buyer workspace directly.
- ☐ All seven Ready areas block incomplete projects.
- ☐ DRAFT and NOT_READY projects never reach Pros or matching.
- ☐ Hard eligibility and capacity checks cannot be bypassed.
- ☐ Every shortlist has proof, explanations and Admin approval.
- ☐ Buyer and Pro accept the same Pact revision.
- ☐ Chat cannot change scope.
- ☐ First Proof and Definition of Done gates cannot be bypassed.
- ☐ Brief and gig requests use the same execution lifecycle.

Commercial and Cashfree gates

- ☐ Every commercial surface shows QuickQuid fee ₹0 correctly.
- ☐ Q₹ cannot be mistaken for money.
- ☐ Cashfree signature, duplicate, out-of-order and mismatch cases pass.
- ☐ Multiple payment attempts remain distinct by cf_payment_id.
- ☐ One accepted milestone creates no more than one payout intent.
- ☐ Easy Split cannot activate escrow wording.
- ☐ UTR, manual bank matching, offline instruments and cheque workflows are absent.

Operations and quality gates

- ☐ Negative authorization tests cover every Admin capability.
- ☐ Maker and checker are different people.
- ☐ Sensitive reveal is reasoned, time-limited and audited.
- ☐ Audit history cannot be edited through the application.

- ☐ Privacy export redacts third-party data.
- ☐ Every core screen includes loading, empty, failure and recovery states.
- ☐ Keyboard, screen-reader, 200% zoom and 320px tests pass.
- ☐ Browser refresh, back, double-click and flaky network do not duplicate transitions.
- ☐ Correlation IDs connect user-visible errors to backend and provider records.

Founding Beta Measures

Measure	Definition
Paid projects	Distinct projects with confirmed real milestone funding; sandbox excluded
Accepted completion	Completed contracts divided by activated contracts eligible to complete
On-time completion	Completed by the current approved Commit Forecast divided by completed projects
First-pass acceptance	Accepted first submissions divided by accepted milestones
Repeat Buyers	Buyers starting another paid project divided by eligible completed Buyers
Delay hours	Recorded hours grouped by Buyer, Pro, QuickQuid and external cause
Dispute rate	Projects with a dispute divided by activated projects
Payout reliability	Settled payouts without manual correction divided by payout attempts
Contribution margin	Revenue less Cashfree, support, verification, dispute and direct service costs
Reconciliation drift	Unexplained difference between internal and Cashfree monetary records

Report counts next to percentages. The founding beta exists to prove accepted outcomes, repeat usage and operational control-not account creation or browsing volume.

Glossary

Term	Meaning
Buyer	Person or organization commissioning work
Pro	Professional delivering work
QuickQuid Ready	Reviewed gate proving a project can enter matching
Proof Match	Relevant evidence linking a Pro to the project archetype
Capacity Lock	Reservation of agreed effort against availability
QuickQuid Pact	Shared agreement covering scope, responsibilities, timing and AI use
Commit Forecast	Evidence-based expected date; not a guarantee
Scope Snapshot	Immutable agreed scope for active work
Change Card	Versioned decision for scope, price or time change
Project Clock	Delay record with owner, duration, evidence and forecast impact
First Proof	Early checkpoint validating shared understanding
Definition of Done	Category-specific delivery and handoff checks
Delivery Vault	Protected milestone evidence and asset-review area
Q₹	Demo-only unit with no cash value
Maker-checker	Separation between recommending and approving a sensitive action
